


## Preliminary Construction Sequencing:

### Sequence One -


The entire perimeter of the Site that fronts along surrounding Roadways are anticipated to be improved per the final Construction documents. Because this Sequence is the flattest part of the Site, the earthwork is less than one fourth of that required for Sequence Two. All pre-installed crypts are to be placed in the median of the drive-ways and earthwork has been factored into Contingency portion of the Earthwork quantities. All the remaining burial excavation spoil that cannot be fully re-used during the backfill and compaction process will be temporarily stockpiled at five locations in the Sequence Two areas adjacent to where additional fill dirt is projected to be required per the Grading plans. These temporary stockpiles will not exceed 10 feet in height.

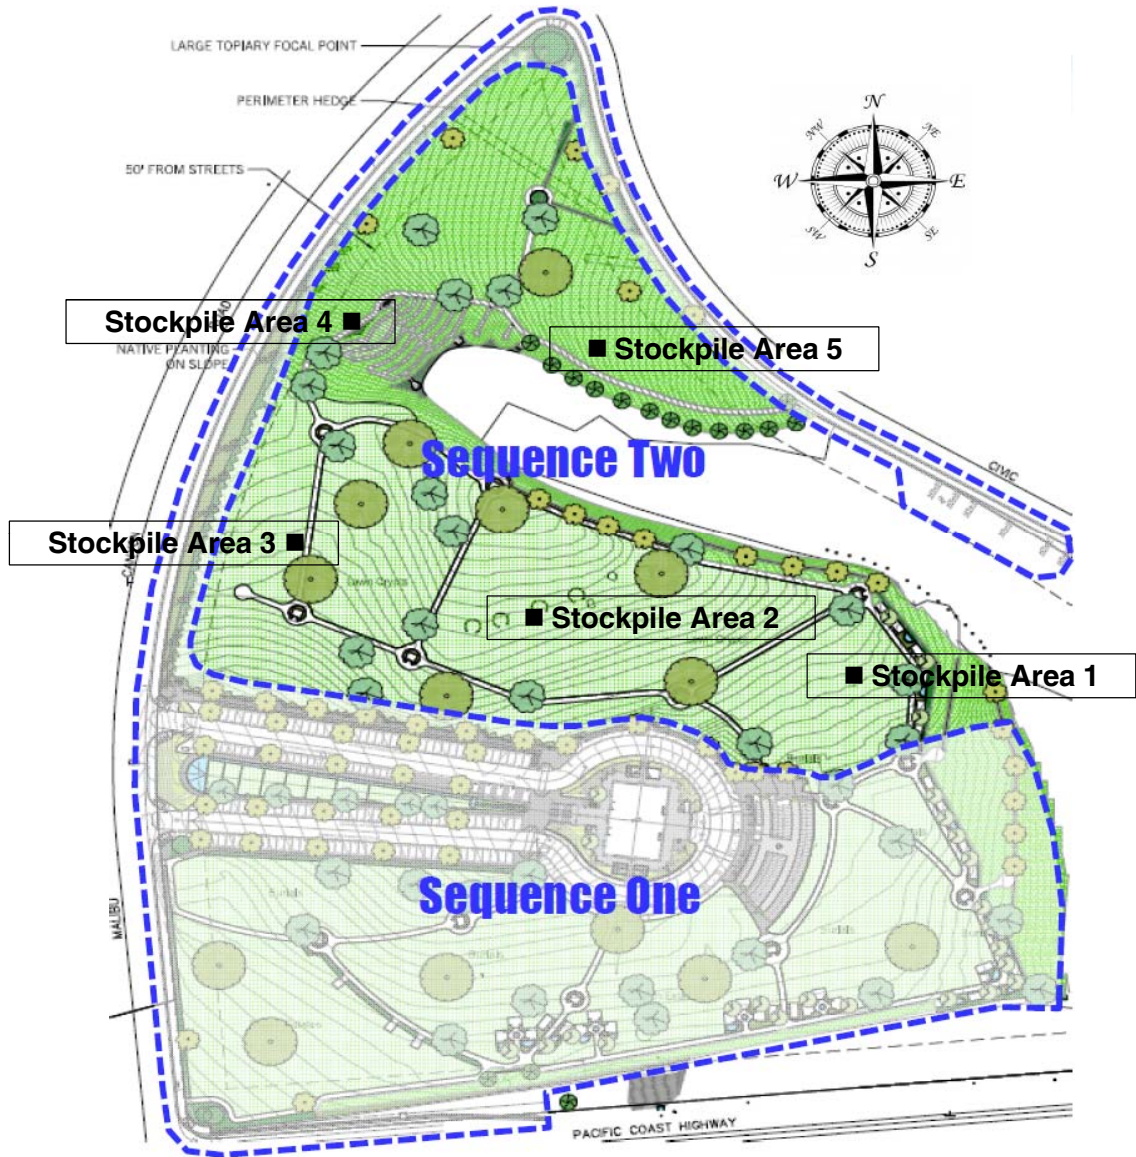

### Sequence Two -

The majority of the Earthwork removal/recompaction work will occur in Sequence Two, as well as the piles that are needed to stabilize the top of the Mesa slope. The excavation spoil stockpiled from Sequence One burials and including the Basement and Public Mausoleum spoil will be needed to balance site per the Grading plan.

Date: 08/04/16



**Malibu Memorial Park**  
4000 Malibu Canyon Rd, Malibu

**Exhibit "C" - Pg 2**  
Preliminary Construction Sequencing

SHEET  
**CS-2**
